



CITY OF CHELAN

WILLMORTH DRIVE TRANSMISSION MAIN CONSTRUCTION PROGRESS REPORT




UPDATED 5/15/20




WATER MAIN INSTALLATION

OVERALL SUMMARY

**WATER MAIN
COMPLETION**

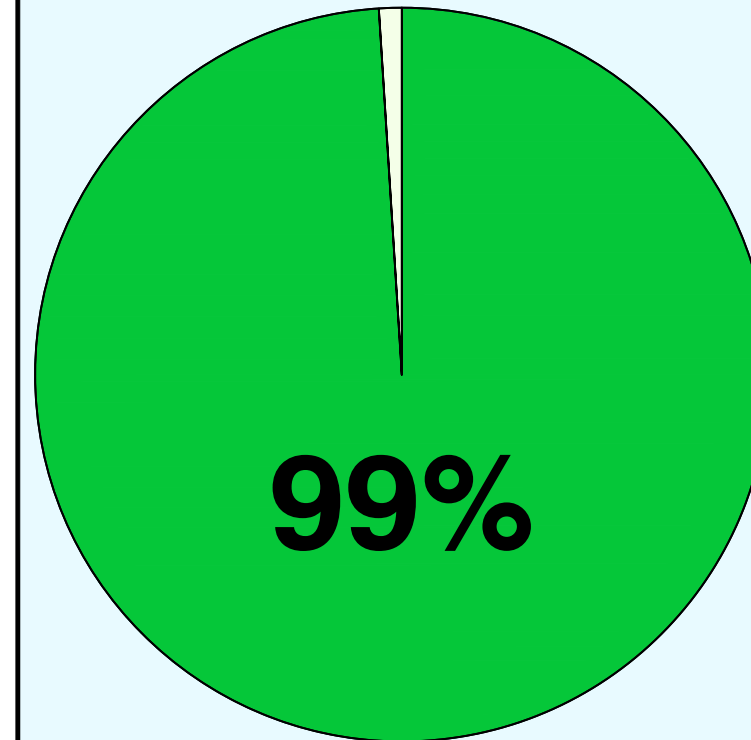

**PROJECT
COMPLETION**

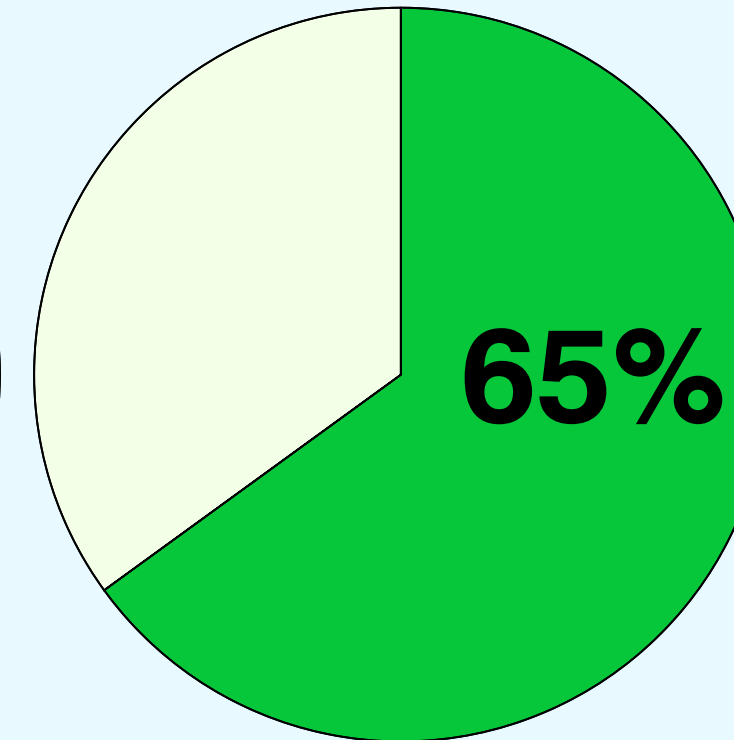

WATER MAIN COMPLETION BASED ON PERCENTAGE OF LINEAR FEET OF PIPE PLACED IN THE GROUND

WATER MAIN PROGRESS

LINEAR FEET OF PIPE

	PLACED & BACKFILLED	TESTED/ COMPLETED
SR 150	218 <hr/> 225	0 <hr/> 225
WILLMORTH DR.	3,315 <hr/> 3,315	0 <hr/> 3,315
ISENHART RD.	1,260 <hr/> 1,260	0 <hr/> 1,260

TRAFFIC ALERTS

WEEK OF MAY 18TH

- WILLMORTH DRIVE AND ISENHART ROAD WILL CONTINUE TO BE CLOSED TO THROUGH TRAFFIC. ACCESS WILL BE MAINTAINED FOR LOCAL TRAFFIC ONLY. CONSTRUCTION ACTIVITIES MAY BE FULLY BLOCKING THE ROAD, BUT ACCESS WILL BE MAINTAINED TO EACH HOME FROM AT LEAST ONE OF THE TWO ENDS OF WILLMORTH DRIVE, SR 150 OR US 97A.

UPCOMING WORK

WEEK OF MAY 18TH

- FILLING AND TESTING THE NEW WATER MAIN
- PLACING ROCK SURFACING

	PROPOSED CONSTRUCTION		TEMPORARY SURFACING
	TRENCH EXCAVATED		FINAL ASPHALT
	PIPE PLACED		TRAFFIC REVISION AREA
	TRENCH BACKFILLED		
	PIPE TESTED/COMPLETED		



INSTALLING NEW WATER SERVICES ON WILLMORTH DRIVE



PLACING A NEW FIRE HYDRANT ON ISENHART ROAD
